

NOTICE OF SERVICE INTERRUPTION/WORK FORM

Date of Request (yyyy/mm/dd): _____		Requester: _____	
Start Date – End			
Start Date (yyyy/mm/dd) _____ Time (s) _____		Notes _____	
End Date (yyyy/mm/dd) _____ Time (s) _____		_____	
Building(s) Affected:	1: _____	2: _____	
	3: _____	4: _____	
Areas/Rooms Affected: _____			
Service to be interrupted:	1: _____	2: _____	
	3: _____	4: _____	
Description/Reason for Project:			
<div style="border: 1px solid black; width: 100%; height: 100%;"></div>			


Contractor: _____	Phone #: _____
Contractor/Project Managers: _____	Phone #: _____

Should you have any questions or concerns, please contact

Notes:

2018-May-23

Lighting Retrofit Project - Chrysler Hall North Type 2 Asbestos Abatement of Lay-in Ceiling Tile

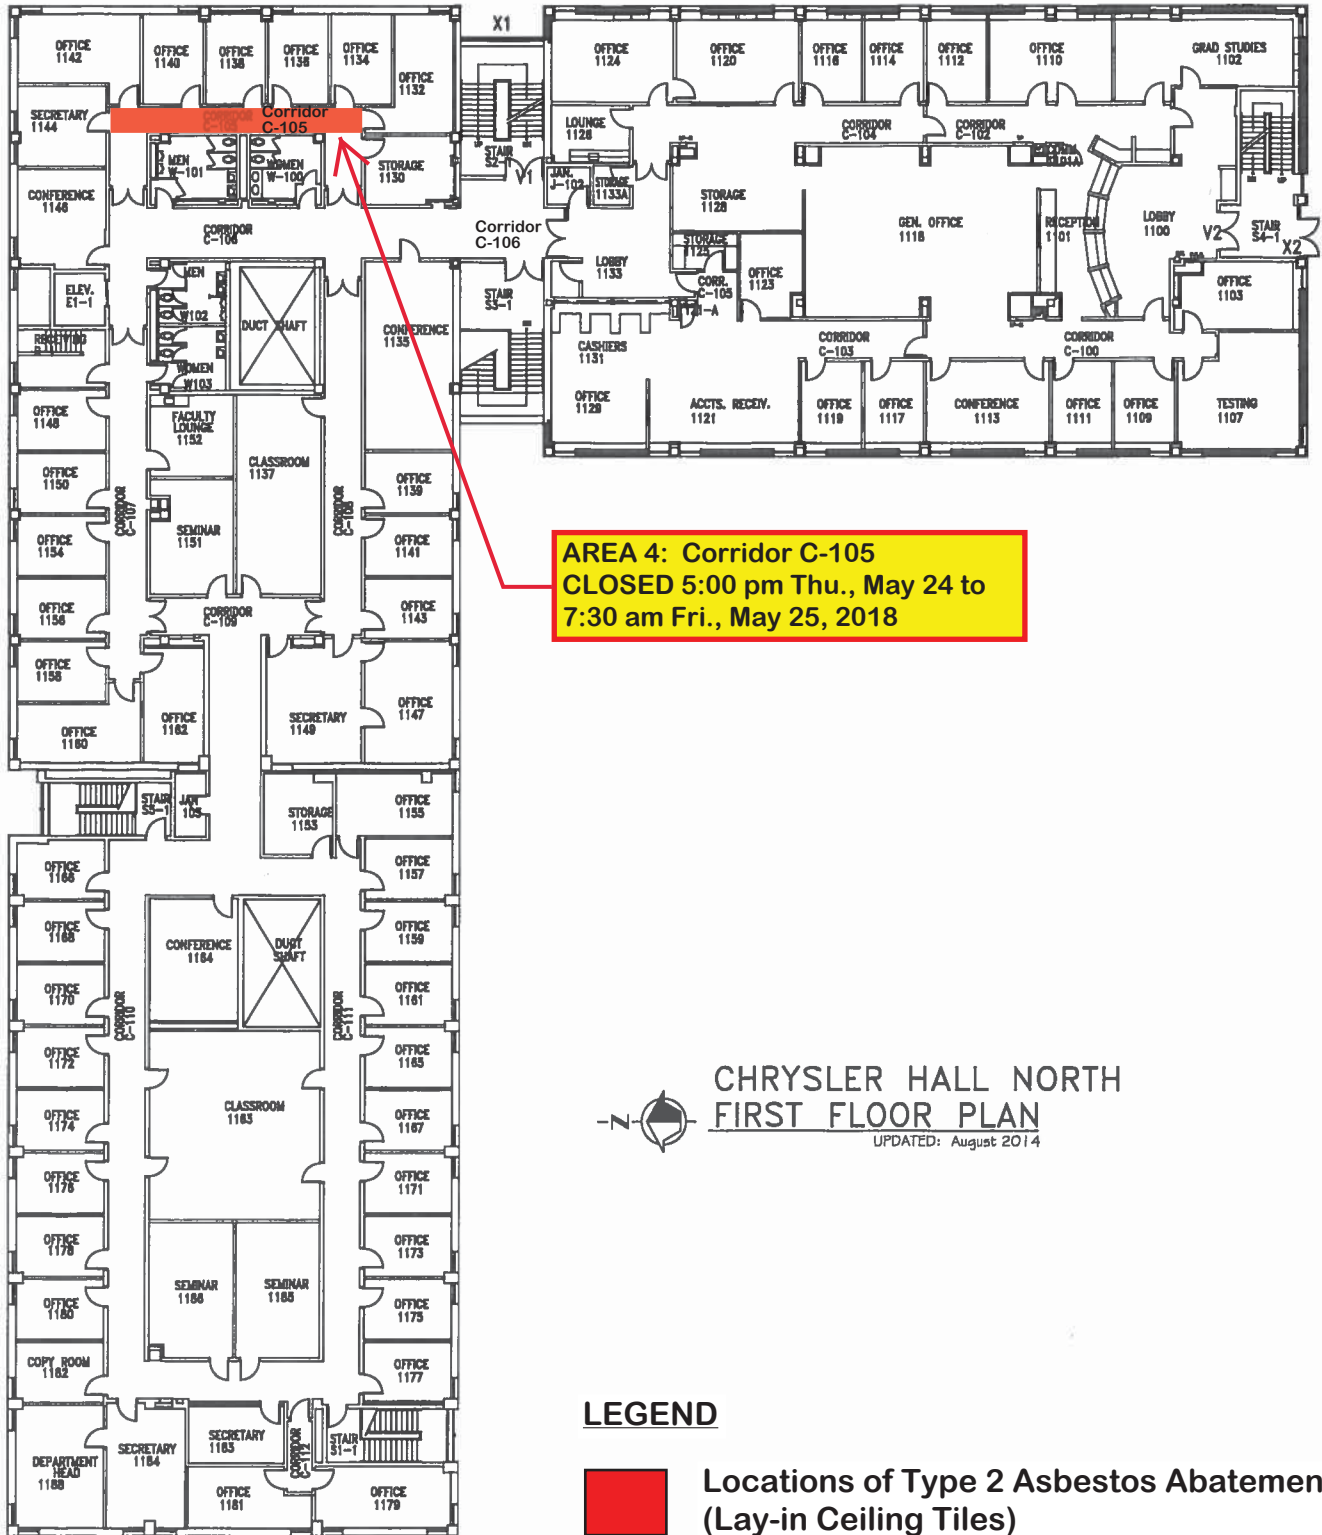

2018-May-23

Lighting Retrofit Project - Chrysler Hall North Type 2 Asbestos Abatement of Lay-in Ceiling Tile





2018-May-23

Campus Lighting Retrofit & Redesign Project

Schedule for Type 2 Ceiling Tile Asbestos Abatement
Chrysler Hall North - Corridors

AREA 4: First Floor Corridor C-105 and Second Floor Corridor C-203

(reference enclosed floor plans)

DATE	Item	TIME	Description of Work	Action By	Done (✓)
Thu., 2018-May-24 To Fri., 2018-May-25	4.1	05/24 - 2pm	Call UWindsor – Heating & Cooling – Control Room (x7027 or 519-973-7027) for air handlers to be turned off. UofW backup contact person: Rob Fontanini 519-890-5369	RC White	
	4.2	05/24 - 4:30pm	Shutdown air handlers. UWindsor to provide lock box to lock out units. Contractor to provide their own locks. Contractor Contact Person: Ted Byrne 519-791-7782	UW-H&C RC White	
	4.3	05/24 - 5pm	Start installing Type 2 enclosures. Post signage at Key Entry points to Abatement Area	RC White	
	4.4	05/24 - 5pm	Call Michelle White for pre-inspection of Areas #4	RC White	
	4.5	05/24 - 8pm	Michelle White to complete pre-inspection of Area #4 enclosures and set up air sampling, c/w email approval	RC White	
	4.6	05/24 – 8:30pm to 05/24 - 10:30pm	Complete abatement work in Area #4: C-105 and C-203	RC White	
	4.7	05/24 – 10pm	Call Michelle White for post-inspection of Area #4	RC White	
	4.8	05/24 – 10:30pm	Michelle White to completed air sampling of both of Areas #4, post-inspection of enclosures to ensure they are clean and free of any asbestos debris, and provide verbal and written approval to dismantle the enclosures c/w report	M. White	
	4.9	05/25 – 7am	Take Type 2 enclosures down, clean up all debris from site, secure building and leave	RC White	
	4.10	05/25 – 7am	Contractor to remove their locks from lockout box	RC White	
	4.11	05/25 – 7am	Call UWindsor – Heating & Cooling – Control Room (x7027 or 519-973-7027) for air handlers to be turned back on. UofW backup contact person: Rob Fontanini 519-890-5369	RC White	
	4.12	05/25 – 7:30am	UWindsor Heating & Cooling to remove their locks and turn HVAC air handling units back on	UW-H&C	

Department/Contractors to Submit Checked-off copy within 24 hours of completion of all work to:

Project Administrator: Roger J. Rivard, UWindsor - Facility Services, E-mail: (mrrj@uwindsor.ca)

End of Schedule

Encl. (2)
