

NOTICE OF SERVICE INTERRUPTION/WORK FORM

| | | | |
|--|----------|-------------------------|--|
| Date of Request (yyyy/mm/dd): _____ | | Requester: _____ | |
| Start Date – End | | | |
| Start Date (yyyy/mm/dd) _____ Time (s) _____ End Date (yyyy/mm/dd) _____ Time (s) _____ | | Notes _____ _____ | |
| Building(s) Affected: | 1: _____ | 2: _____ | |
| | 3: _____ | 4: _____ | |
| Areas/Rooms Affected: _____ | | | |
| Service to be interrupted: | 1: _____ | 2: _____ | |
| | 3: _____ | 4: _____ | |
| Description/Reason for Project: | | | |
| <div style="border: 1px solid black; width: 100%; height: 100%;"></div> | | | |

| | | | |
|---|--|-----------------------|--|
| Contractor: _____ | | Phone #: _____ | |
| Contractor/Project Managers: _____ | | Phone #: _____ | |

Should you have any questions or concerns, please contact

Notes:

U of W St. Denis & Human Kinetics Greenhouse Gas Retrofit Project

St. Denis Centre Fieldhouse Lift Plan (Hoist #1)


Thursday December 20th, 2018

Procedure: AHU 4

- Moir Crane Service will hoist AHU 4 at the rear of the fieldhouse (see attached overhead view for crane position and lift radius)
- The rear project parking will be closed to all other trades until apx. 12:00 pm
- The fieldhouse will be closed to all personal until 3pm.
- Vollmer will have the crane area taped off and will provide ground personal to control the flow of vehicle and people traffic

Procedure: AHU 6

- Moir Crane service will supply and place the ground plating to protect the concrete and landscaping on the NE side of the St. Denis Main Entrance
- Cameron Crane Service will hoist AHU 6 from truck to position (see attached overhead view for crane position and lift radius)
- The St. Denis Lobby and rooms east of the Lobby will be closed until 3 pm.
- The fieldhouse will be closed to all personal until 3pm.
- Vollmer will have the crane area taped off and will provide ground personal to control the flow of vehicle and people traffic

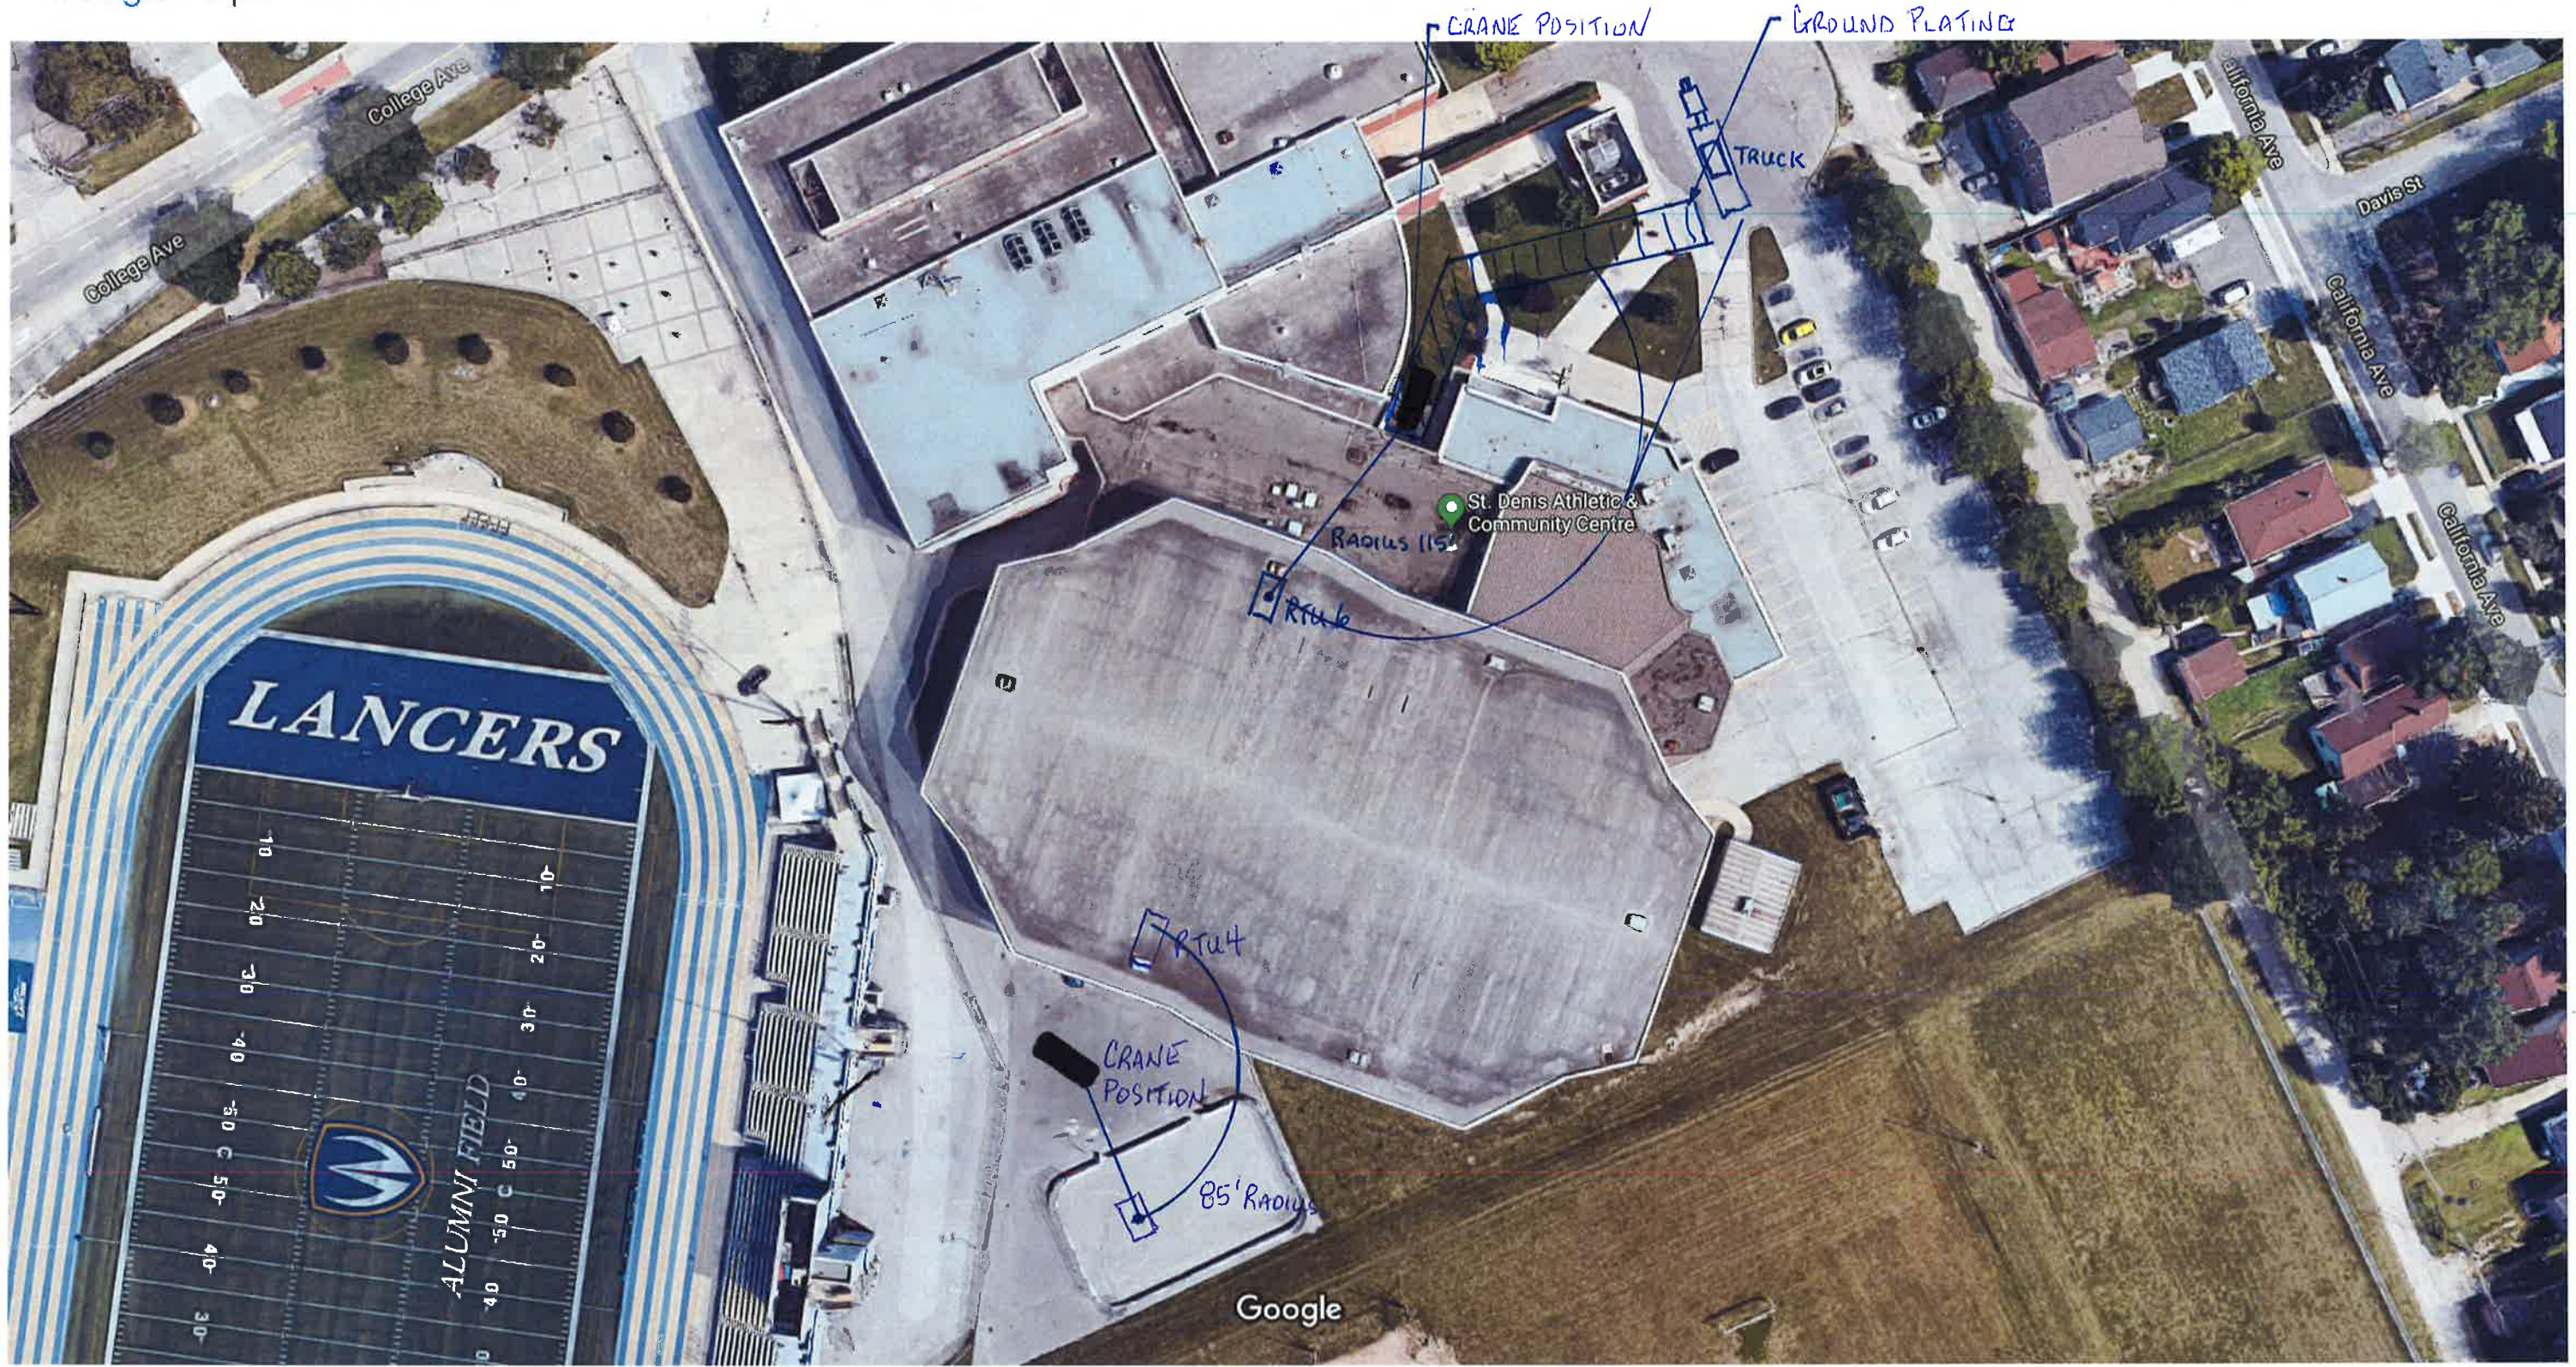

[Set a home address](#)
